



CONNECT. GROW. FIGHT TOGETHER.

Milestones 1, 2 and 3. What has been delivered.

An evidence-backed account of the work Momentum Digital has researched, designed, built, tested and deployed for Bridge across the first three contract milestones – the discovery and architecture foundation, the UX and data-model system now live for review, and the accounts, authentication and verification milestone currently in progress.

Prepared

September 3, 2026

Evidence window

May 27 – September 3, 2026

StatusMilestones 1–2 delivered ·
Milestone 3 in progress

Two milestones delivered. The third is built, tested and waiting on the backend contract.

Bridge has a documented product direction, a role and permission model, a thirteen-route front end live on two deployment environments, and a complete reference implementation of the account, sign-in and verification surfaces. Milestone 3 is not finished: the frontend half is built and passing continuous integration, and the remaining work is the backend data contract that Greencubes owes before the screens can bind to real accounts.

13

ROUTES VERIFIED LIVE IN PRODUCTION

45

AUTOMATED TESTS PASSING

12

MEMBER ROLES DEFINED AND BUILT

2

DEPLOY ENVIRONMENTS RUNNING

What is complete now

- Product requirements, role definitions and MVP boundary agreed and written down
- Architecture and data-model direction delivered, with the compliance and verification inputs translated into product questions
- Five reviewable product routes live and QA'd on the client review URL
- Role and field permission matrix separating public, member-only and protected data
- Twelve-role join entry, admin verification queue and nationwide discovery built
- Integration pipeline and API contract published and handed to Greencubes

What is next

- Tori's route-by-route accept-or-revise on the five review routes
- Product approval on Join Steps 2 and 4 — the organization detail and verification review screens
- Greencubes to supply the session claims, route table and storage contract that Milestone 3 depends on
- Merge the Milestone 3 hardening branch once the backend contract is settled
- Verification policy decision: what evidence each role must provide
- Milestone 4, the Directory MVP, has not started

The front end is real; the data behind it is not yet

Every screen on the review URL runs against a typed mock adapter, and each one says so on the page. That was deliberate: it let the product be reviewed and approved before backend cost was committed. Turning mock mode off is a single environment variable, and it waits on Greencubes returning the backend repository, branch, commit and staging origin.

One vocabulary warning worth carrying into the meeting

In the signed proposal, "Phase" and "Milestone" are the same word — six milestones, six phases, one numbering. The engineering build specification uses "Phase" for something different and unrelated. This report uses the contract's own vocabulary only, and names each milestone in full, so no number is ambiguous.

What happened, in order.

Dated from the executed NDA through to this report. Each entry is traceable to a Slack message, an email thread, a commit or a deployed build.

MAY 27 • NDA drafted, circulated and signed

Mutual NDA executed across the client, Momentum and the engineering vendor; fully executed June 1. Product still named "The Ecosystem" at this point.

JUN 2-8 • Scope written as six milestones

The proposal was drafted, reviewed and updated — six milestones from discovery to launch, with client-side pass-through costs and a project team section added.

JUN 7 • The product is renamed Bridge

Tori renames The Ecosystem to Bridge. The six-milestone structure is approved by the engineering vendor the same week.

JUN 11 • Agreement finalised and sent to the client

Terms covering NDA, non-compete, ownership, rights and phases were added and the agreement was issued for signature.

JUL 8 • Contract approved • Milestone 1 starts

Client green light. The **#bridge-software-development** channel is created the same afternoon and Milestone 1 is opened.

JUL 10-16 • Execution plan, six-milestone brief and decision register

Momentum's execution plan and the engineering vendor's six-milestone plan were published, followed by the canonical milestone decision brief recording verified decisions, open requirements, owners and the approval gate.

JUL 19-20 • Client source package received • onboarding walkthrough

Tori supplies four original HTML concepts, the Bridge branding guide, the business verification requirements and the legal/compliance platform strategy. The prototype walkthrough call runs the next day and a working prototype ships hours later.

JUL 27 • Milestone 1 architecture document delivered

The architecture and platform plan is delivered by the engineering vendor and forwarded to the client. Milestone 1 is paid at the end of that month.

AUG 1-7 • Tori's written feedback drives the Milestone 2 plan

A 39-minute recorded product session and written notes are supplied by the client and converted into the Milestone 2 execution plan — with the foundation confirmed rather than reworked. The acceptance record is opened with every item explicitly pending, and the build is posted for review.

AUG 14-17 • Milestone 2 completes • conditional acceptance issued

The backend schema, roles and permission model are reported complete; Momentum's own review returns *conditional acceptance pending evidence and security remediation*. The five-route front end is completed and sent to the client for sign-off on August 17.

AUG 21 • Milestone 3 opens • 21+ entry gate restored

Accounts, authentication and verification work begins. The adult-entry confirmation is restored ahead of every route on the review build.

AUG 31 • Integration pipeline and API contract published

The frontend repository, branch model, CORS origins, endpoint contract and security rules are written down and handed to Greencubes. Repository and hosting invitations are issued.

SEP 2-3 • Backend delivery reviewed • Milestone 3 hardening built

The Greencubes auth and admin delivery is reviewed against the contract; the Milestone 3 hardening branch restores the join sequence, unifies the HTTP client, adds required states, accessibility fixes and continuous integration. All checks pass.

The foundation: what Bridge is, who it serves, and how it is built.

Milestone 1 turned an idea and a set of client-authored concepts into a documented product with named roles, an agreed MVP boundary, a technical architecture, and a compliance intake translated into product requirements. **Status: delivered and paid.** The technical plan and research findings were delivered on July 27 and the client's written response on August 5 was *"the specs are awesome, the research is top tier"* — warm, but not a formal milestone acceptance. No dated acceptance artifact was recorded, which is worth closing retrospectively.

What was researched and decided

- The MVP boundary — what ships first and what is deliberately deferred
- The contracted core user set: brands, retailers and dispensaries, sales representatives, and administrators
- Priority journeys per role, and the low-fidelity flow direction validated before any visual polish
- The ownership split between front-end delivery, UX, backend integration and final acceptance
- A written exclusion list — algorithmic feed, advanced social graph, native mobile apps, recommendation engine, in-platform payments, subscriptions and marketplace ordering are all outside this build

The architecture put in place

- Browser-based, role-based platform: Next.js, React and TypeScript on the front end
- PostgreSQL with row-level security as the data and permission substrate
- Git-linked continuous deployment to two hosted environments
- A private source repository with an explicit branch model and review gate
- An open decision register carrying every unresolved product question with a named owner and a decision-by point

The prototype families and the brand source

INPUT	WHAT IT WAS AND WHAT IT BECAME
Momentum discovery prototype	A working Next.js prototype family built to make the product reviewable in the walkthrough — role-based journeys, core screen direction and build-ready front-end requirements. Became the codebase the product now runs on.
Client concept set	Four original HTML concepts supplied by Tori — landing and signup, dashboard and feed, post designer, and directory and profiles. Preserved, extracted, indexed and used as the product-intent source of record.
Bridge branding guide	The client's own brand source. The Bridge arch mark, the wordmark and the "Connect. Grow. Fight Together." line carried through into the built product rather than being redesigned.
Business verification requirements	The client's compliance document. Converted into the EIN, licence-status and jurisdiction fields, the account approval states and the admin verification queue that Milestone 3 implements.
Legal and compliance platform strategy	Drove the 21+ adult-entry requirement, the protected-field boundary between public and business-only data, and the rule that no EIN document is ever publicly visible.

Compliance shaped the product, not just the paperwork

The verification and legal inputs were not filed away — they became structural. Three things in the live product exist because of them: the 21+ confirmation that blocks every route before entry, the two-mode profile that separates what the public sees from what verified businesses can access, and the admin queue that treats verification as a reviewable case with a status and a waiting time rather than a checkbox.

The product system: screens, roles, journeys, states and the data behind them.

Milestone 2 produced the application map, the core user flows, the profile structures for each business type, the taxonomy, the admin review workflow, the database schema and the permission model — and then built five reviewable routes so the client could judge the product rather than a document. **Status: delivered and live for review; client route-by-route sign-off is still outstanding.**

The five review routes and what each one does

ROUTE	WHAT IT DOES	ACCEPTANCE
Home	Compact product introduction with legal cannabis positioning, a single primary join action, and one-click access to the four primary spaces.	PENDING TORI
Community News	The same items presented as either a visual News Grid or a classic chronological feed, with category and state controls, favourites, and an explicit selected state. Non-algorithmic by design for the MVP.	PENDING — DEFAULT VIEW UNDECIDED
Create	Promotion and message composition with content type, upload validation, multi-audience selection, a protected-detail guardrail that removes public targeting automatically, and live preview.	PENDING TORI
My Profile	Two projections of one record — Public view and B2B verified view — with protected sales and accounting contacts, no public EIN, and a required first-login and monthly contact confirmation gate.	PENDING TORI
Explore	Nationwide discovery across all fifty states and D.C. with category and role filters, a visible result count, persisted favourites, and an explicit permissioned introduction request.	PENDING TORI

Data model and permissions

- PostgreSQL schema with organization isolation, tables, relationships, constraints, indexes and migration history
- Row-level security policies and a role permission model reported complete by the engineering vendor
- A role and field permission matrix defining, per field, whether it is public, member-only or protected
- Product and category taxonomy, and search and filter requirements
- Admin review workflow design — the queue, its statuses and its decision points

The handoff package

- Route and screen map
- Role and field permission matrix
- Journey maps with acceptance criteria per route
- Phased backlog and decision register
- A one-page engineering handoff summarising the contract the backend must satisfy
- A route-by-route acceptance record with an empty decision column per route — nothing marked without a dated source


Honest status on Milestone 2

The frontend half is built, deployed and QA'd on desktop and mobile. The backend half was reported complete and Momentum's own review returned **conditional acceptance pending evidence and security remediation** — repository, branch, commit and migration evidence were requested and are still outstanding, and a credential exposure in the shared channel required rotation before formal acceptance.


No client acceptance is claimed here, because none has been recorded. The build was sent for sign-off on August 17. A review was promised on August 18, again on August 23, and again on September 1. On August 21 Momentum wrote to the client, in writing, that *the five routes are not officially approved yet*. The acceptance record's decision column remains empty for all five routes today.

The review build, as it stands today.


Captured at 1440 px from **bridge-connected-signal.netlify.app** on September 3, 2026. Every route below returned HTTP 200 at capture time.

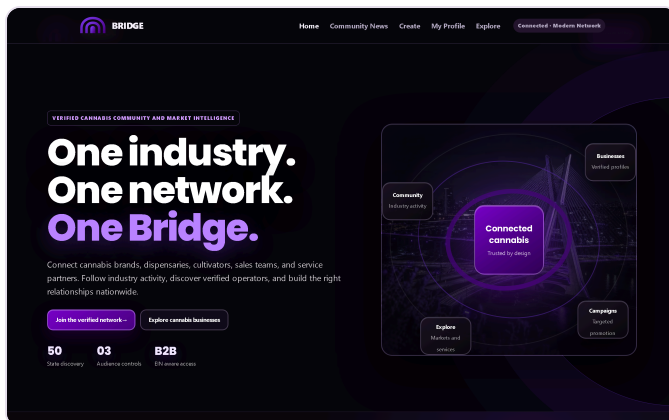


HOME — POSITIONING AND PRIMARY JOIN ACTION

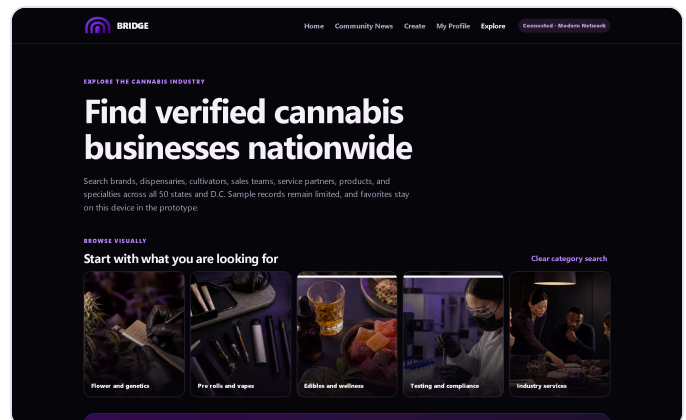


EXPLORE — NATIONWIDE DISCOVERY, 50 STATES + D.C.

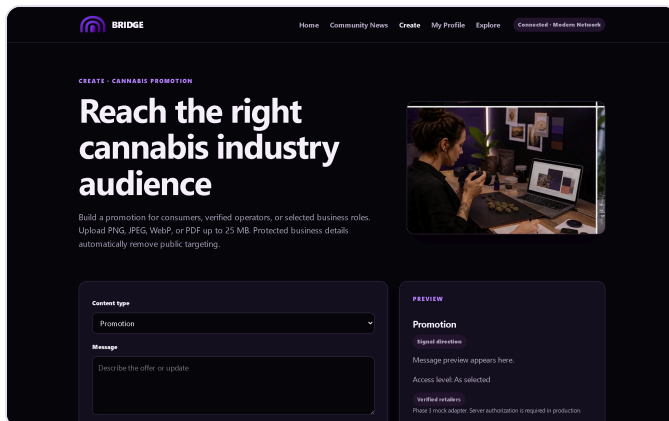

CREATE — AUDIENCES AND THE PROTECTED-DETAIL GUARDRAIL

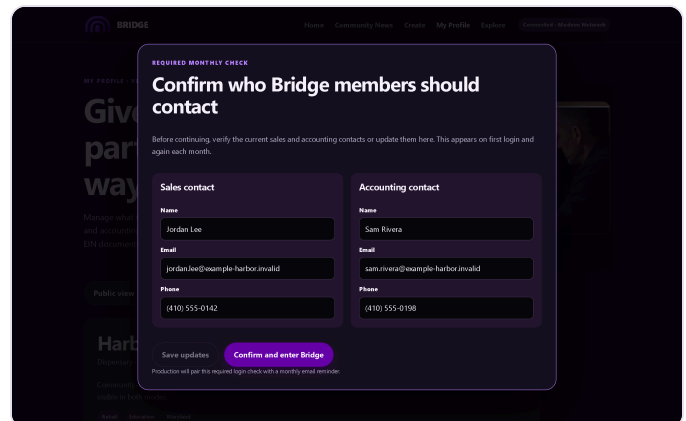

MY PROFILE — PUBLIC VS. B2B VERIFIED PROJECTION

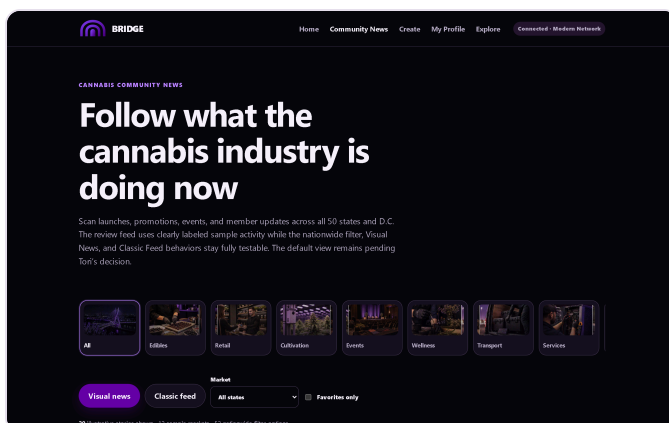

COMMUNITY NEWS — NEWS GRID AND CLASSIC FEED, BOTH BUILT

Every screen states its own boundary

Explore says sample records are limited and favourites stay on the device. Create says draft, library and review actions remain local until the production API is connected. My Profile says the email reminder integration is pending. Nothing on the review build implies a capability that is not there.

Responsive behaviour verified

Each route was captured at both 1440 px and 390 px on the same day. Navigation collapses to a menu, the multi-column grids reflow to single column, and no route scrolls horizontally at mobile width.

In progress. The front end is complete; the backend contract is the open half.

Milestone 3 owes registration and login, email verification, password reset, role-based accounts, EIN capture, state and licence-status fields, account approval status, an admin verification queue, and privacy and terms acceptance. Momentum has built the complete frontend reference implementation of that surface. Greencubes has delivered a genuinely secure backend with real server-side role checks, describing their own side as half done on August 29 and almost done on September 2, with a final update due. The two halves do not yet meet.

The join sequence, as designed

STEP	ROUTE	WHAT IT CAPTURES	STATE
Step 1 of 4	/join	Member role — a twelve-role grid with per-role next-step titles and requirements, the founding-member callout, and the boundary note explaining what Steps 2–4 need.	LIVE IN PRODUCTION
Step 2 of 4	/join/account	Account creation — display name, email, password and confirmation, showing the role chosen in Step 1 with a link back to change it. Full inline validation and error states.	BUILT · PENDING MERGE
Step 3 of 4	—	Organization details — legal name, public name, EIN, licence, location and contact owner. Requires organization-scoped draft persistence.	AWAITING BACKEND + APPROVAL
Step 4 of 4	—	Verification evidence and review submission — server-created upload intents, document scanning, a redacted review summary and a verification case.	AWAITING BACKEND + APPROVAL

Steps 2 and 4 need a product decision from Melissa and Tori

Step 1 is deliberately the only step live in production. Steps 3 and 4 are not missing routes or a hosting problem — they need a real member identity, organization-scoped drafts, protected evidence storage and a review case, all of which are backend-owned. They also need a product answer on **what verification evidence each of the twelve roles must supply** and **what the public "Verified" badge promises**.

This has been stated plainly to the whole team, in writing, since August 31: *Step 2 and Step 4 product approval is still with Melissa and Tori — do not represent those screens as client approved*. That instruction still stands today, and this report holds to it.

One HTTP client, one contract

Registration, sign-in and sign-out were added to the same typed client every other call already uses — so they inherit one base URL, one status mapping (401 unauthenticated, 403 forbidden, 400/422 validation, 409 conflict) and one error type. A second, parallel HTTP client that had bypassed that contract was folded back in.

A mock fallback means sign-in and account creation work with no backend at all, which is what makes the flow reviewable today.

Session handling and role-aware routing

- No token in browser storage — the session is read from the API on each load, as a cookie session requires. A test asserts no client file touches web storage
- Sign-in sends members to their profile and administrators to the admin workspace
- The return-path parameter accepts only same-origin paths; absolute URLs and protocol-relative hosts are rejected
- Every routing rule carries an explicit note that client-side routing is presentation only and never authorization — the API must still enforce it

Every required state, measured contrast, and a build that now checks itself.

Required states across every route

One shared component now covers loading, empty, error, forbidden, unavailable and retry, with the correct assistive-technology roles and busy states. Error text is filtered: only a curated user-facing message is shown, so an internal error, a stack or a raw backend string can never reach the screen.

- Sign-in never distinguishes "no such account" from "wrong password"
- A permission denial offers no pointless retry; a service outage does
- Explore shows a visible notice when browser storage is unavailable instead of failing silently
- The admin queue has a real empty state with a reset action

Accessibility, measured not asserted

An automated check implements the published contrast formulas, reads the colour tokens directly out of the stylesheet so measured values can never drift from what ships, and asserts the AA threshold for every rendered text-on-background pair in all three themes.

- **Five** contrast failures in the admin panel fixed — the worst was 2.88:1 against a 4.5:1 requirement
- **Two** further failures found in the existing theme tokens that nobody knew about, including form error text at 2.22:1 — effectively unreadable — now 6.02:1
- The keyboard skip link, previously hidden on admin pages, is present again
- Sidebar controls given 44 px minimum touch targets; reduced-motion preference respected

Verification gates — baseline against the Milestone 3 branch


GATE	BEFORE	AFTER
Automated test suite	24 passing	45 passing, 0 failing
Type check	Pass	Pass
Lint	Pass	Pass
Production build	33 static pages	36 static pages
Continuous integration	None existed	Runs on every pull request
Raw colour values in the admin panel	~110 lines of hard-coded hex	Zero, asserted by test

Why continuous integration mattered here


The repository had no automated checks at all, which is how a branch with a failing test reached a pull request in the first place. Install, test, type-check, lint and build now run automatically on every pull request into the development and production branches. The build step deliberately pins the API origin empty, so each run proves the documented no-backend default still builds. Twenty-one new tests cover the twelve-role catalogue, the role round-trip from Step 1 to Step 2, post-sign-in landing paths, the open-redirect guard, the unified client, and the complete account-creation flow with no backend.

The surfaces Milestone 3 owns.


Desktop captured at 1440 px, mobile at 390 px, both from production on September 3, 2026.

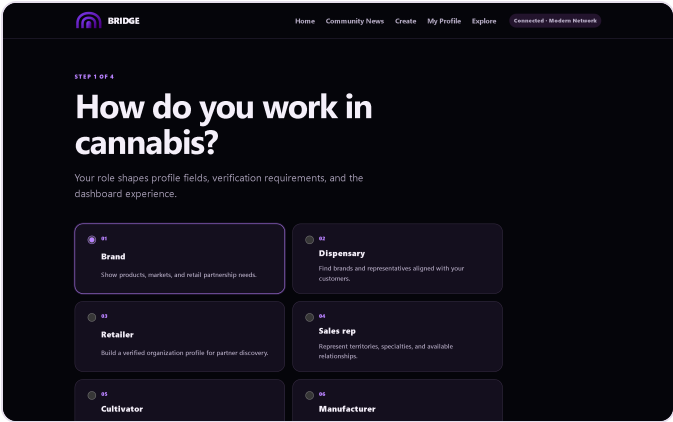


JOIN, STEP 1 OF 4 — THE TWELVE-ROLE GRID LIVE IN PRODUCTION

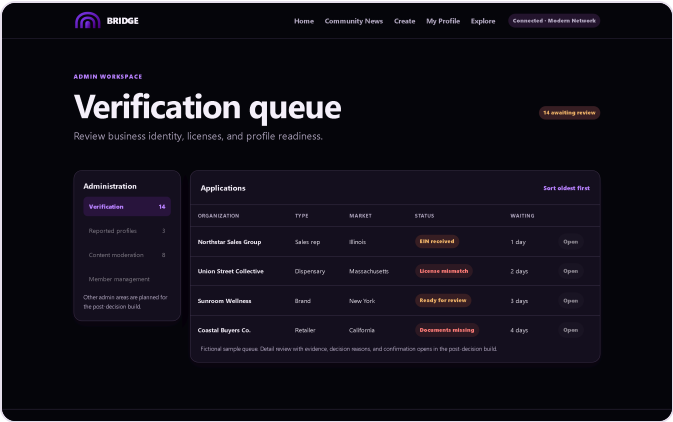


ADMIN VERIFICATION QUEUE — CASES, STATUS AND WAITING TIME

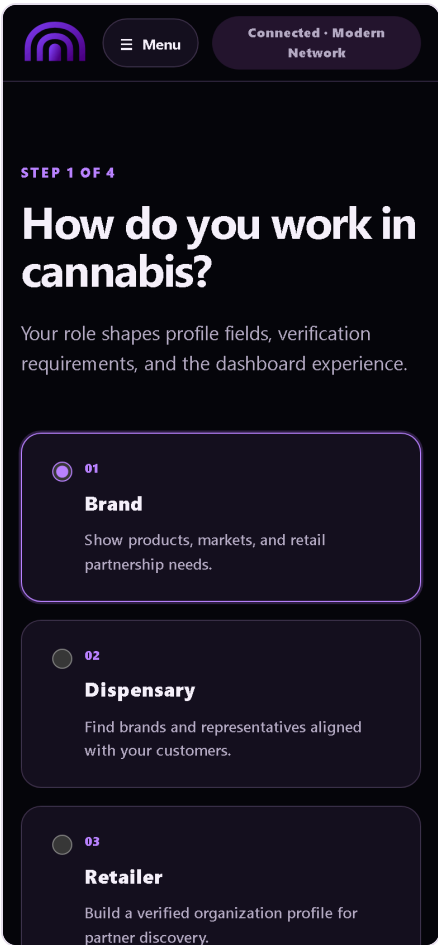

JOIN · 390 PX

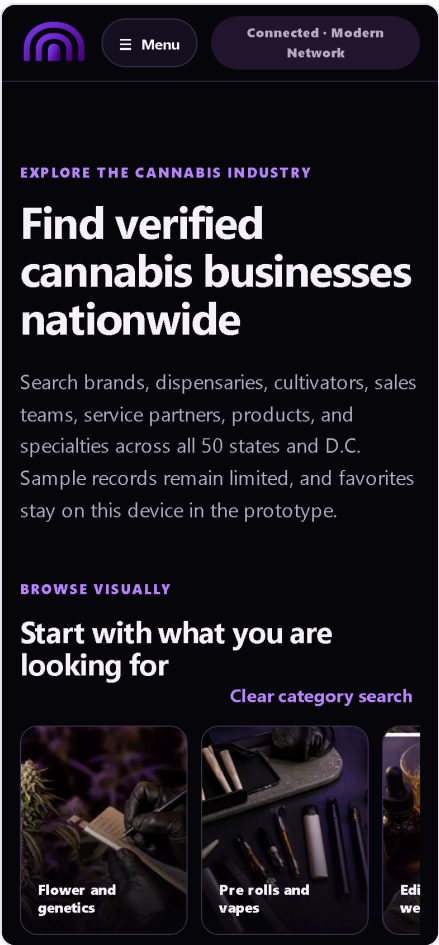

EXPLORE · 390 PX

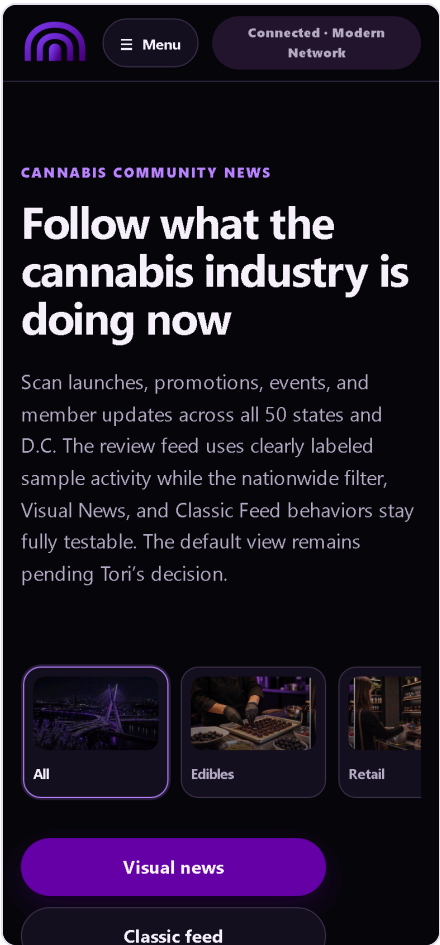

COMMUNITY NEWS · 390 PX

What the admin queue shows, and what it does not yet

The queue renders real case rows — organization, type, market, verification status and days waiting — with a sortable order and a live count. It is running on a clearly-labelled sample queue. Case detail with evidence, decision reasons and confirmation is the part that needs the backend's verification-case contract, which has not been supplied.

Every number below was checked directly, not carried forward from a report.

13

ROUTES RETURNING HTTP 200 IN PRODUCTION

3

LEGACY PATHS REDIRECTING CORRECTLY

45

TESTS PASSING, ZERO FAILING

36

STATIC PAGES IN THE PRODUCTION BUILD

7

CONTRAST FAILURES FOUND AND FIXED

3

THEMES CHECKED FOR AA COMPLIANCE

15

PULL REQUESTS OPENED, 9 MERGED

77

COMMITTS ON THE DEVELOPMENT BRANCH

Source for each number

METRIC	VALUE	HOW IT WAS VERIFIED
Routes live in production	13	Direct HTTP probe of every route on bridge-connected-signal.netlify.app, 2026-09-03. All returned 200.
Legacy redirects	3	Same probe: /studio→/create, /business→/my-profile, /signal→/explore, each a 301 to the correct target. Confirmed again in a live browser.
Deploy environments	2	Production and preview both probed; the identical route set and redirect behaviour returned on both.
Tests passing	45	Recorded in the Milestone 3 build report from a clean install, and independently re-run by continuous integration on the pull request.
Static pages built	36	Production build output on the Milestone 3 branch, against 33 on the baseline.
Continuous integration	Passing	Four workflow runs on the Milestone 3 pull request, all successful; the combined test / type-check / lint / build check completed in 44 seconds on the most recent run.
Contrast failures fixed	7	Five in the admin panel plus two pre-existing theme-token failures, each with a measured before-and-after ratio in the build report and asserted by an automated check.
Themes verified	3	Modern Network, Trusted Current and Botanical, each asserted against the AA threshold by the automated contrast test.
Member roles	12	Counted on the live /join screen and in the shared role catalogue that both join steps read from.
Geographic coverage	50 states + D.C.	State selector enumerated on the live Explore route.
Pull requests	15 opened · 9 merged	Repository pull-request history, 2026-08-31 to 2026-09-03.
Commits on development	77	Commit count on the development branch, first commit 2026-07-11.

Route counts refer to distinct application routes reachable in production. The static-page count is higher because it includes generated profile pages. Three routes built in Milestone 3 — sign-in, account creation and the admin entry redirect — are not counted as live: they return 404 in production today because the branch that adds them has not been merged.

What the front end promises the backend, and what is still outstanding.

Two documents were published on August 31 and handed over: an integration pipeline describing repository ownership, the branch and review model, hosting, access and the security rules; and an API contract naming every endpoint the front end already calls, with request and response shapes and the exact status mapping expected.

Delivered and independently verified

- Server-side role enforcement that correctly rejects both missing and forged credentials on every protected route
- A real cross-origin allowlist naming the exact production, preview and local origins, returning nothing for an unknown origin
- Strong response security headers and a consistent error envelope
- Working health and version endpoints
- Registration, sign-in, password recovery and email re-verification screens
- An admin verification queue sending filters as real server-side parameters

Outstanding before Milestone 3 can close

- Six of the nine required session claims are absent — including the age-eligibility signal that the 21+ gate depends on, which today has no server-authoritative source
- One missing response header currently prevents cookie sessions from working; it is the single root cause behind three separate defects
- Access and refresh tokens are being written to browser storage, against the written security rule
- No route table or response examples, so the front end defensively probes several possible response shapes
- The verification-case contract — paginated cases, case detail, evidence references, decisions with reason codes and audit events
- Backend repository, branch, commit and staging origin — the precondition set on August 31 for turning mock mode off
- Storage rules: buckets, file types, size limits, signed URLs and retention

One approved screen was replaced and has been restored

The backend delivery removed the Join Step 1 role grid and replaced it with a sign-up card. That deleted the only place the product captures a member's role — which the organization onboarding and the verification flow both depend on — and removed the exact screen whose Step 2 and Step 4 product approval is still open with the client. Rather than reverting the work, both screens were kept: Step 1 remains the entry point unchanged, and account creation became its own Step 2. Nothing was lost on either side.

The security posture is the strongest part of the backend delivery

Real server-side role checks, a correct origin allowlist and strong headers are the hard parts and they are done properly. The outstanding items above are contract and documentation gaps, not architectural ones, and they are inexpensive to close.

Three lanes, three owners.

Milestone 3 closes when the backend contract lands and the product decisions on the join flow are made. Nothing below is blocked on more than one party.

WITH GREENCUBES

The backend contract

- Add the one missing response header that restores cookie sessions
- Move access and refresh tokens out of browser storage
- Supply the six missing session claims, age eligibility first
- Reconcile the two session endpoints and settle one shape per concept
- Publish the route table and the verification-queue response schema
- Return backend repository, branch, commit and staging origin
- Move admin search and filtering server-side
- Confirm the Milestone 2 credential rotation is complete

WITH THE CLIENT

Product decisions

- **Route-by-route accept or revise** on all five Milestone 2 routes — this is the outstanding acceptance
- **Join Step 2 and Step 4 product approval** — Melissa and Tori
- Default Community News view: News Grid or classic feed
- What evidence each of the twelve roles must supply for verification
- What the public "Verified" badge promises
- Which profile and contact fields are public, member-only or protected
- First market and priority role for launch
- Formal brand approval of the purple direction already in production

WITH MOMENTUM

Delivery

- Merge the Milestone 3 hardening branch once the backend contract is settled
- Settle the session transport decision with Greencubes
- Bind the front end to the staging origin and turn mock mode off
- Build Join Steps 3 and 4 once approved
- Make age eligibility server-authoritative
- Update the integration contract and pipeline documents as the backend lands
- Keep one canonical milestone map so no number is ambiguous

The single most useful thing that can happen this week

A dated, written accept-or-revise on the five review routes. Everything downstream — Join Steps 3 and 4, the directory work, the verification policy — currently waits behind a product decision rather than behind engineering capacity. The build is ready for it.

Milestone 4 has not started

The Directory MVP is the next contracted milestone and no work has begun on it. The Explore and profile screens on the review build are Milestone 2 UX running on sample data — they are not a directory. Production directory data, connected search, the claim and correction workflow and contact-request routing are all Milestone 4 scope.

How this report was assembled.

Nothing in this document is reported from memory. Every status, count and claim traces to a live check, a repository artifact, a deployed build or a dated message. Where evidence was missing, the report says so rather than filling the gap.

What was checked directly

- Every production and preview route probed for status and redirect behaviour on 2026-09-03
- Each screen walked in a live browser and its content read, at desktop and mobile widths
- All screenshots in this report captured from production the same day
- Repository history, pull requests and continuous-integration results read from source
- Test, build and accessibility figures taken from a clean verified run and re-confirmed by automated checks

Stated limits

- No client acceptance is claimed anywhere in this report, because none has been recorded with a date and a source
- Milestone 1 was delivered and paid, but its formal acceptance was never captured as an artifact
- The Milestone 2 backend was conditionally accepted pending evidence that is still outstanding
- Milestone 3 is in progress. Its frontend work is built and passing checks but is not merged and not live
- Milestone 4 and everything after it has not started

**BRIDGE**

CONNECT. GROW. FIGHT TOGETHER.
