

BRIDGE



THE FUN VERSION

Three milestones, one very long summer.

The serious thirteen-page report has every receipt in it. This is
the same truth, with better lighting and a robot.

Momentum Digital, for Tori • 3 September 2026 • Evidence window 27 May to 3 Sept

Companion to the Milestones 1 to 3 Delivery Report. Every number on
this page matches that one exactly, including the awkward ones.

Four milestones. Two done, one half-built, one untouched.

No number on this page is rounded up and no status is nudged forward. If it says in progress, it is in progress.

MILESTONE 1

Discovery, Requirements and Architecture



● Delivered and paid

Your four concepts, the branding guide, the verification requirements and the compliance strategy became the actual product spec. That spec set the roles, the MVP boundary, the architecture, and the rules now baked into every screen.

Warmly received. "The specs are awesome, the research is top tier." It was never captured as a dated acceptance, though. Worth closing retrospectively.

MILESTONE 2

UX, Product Flow and the Data Model



● Delivered • live for review

Home, Community News, Create, My Profile and Explore are all built, deployed and QA'd on desktop and mobile, with the schema and permission rules behind them.

Not signed off. The acceptance record's decision column is still empty for all five routes. That is the one thing this whole page is quietly asking for.



MILESTONE 3

Accounts, Authentication and Verification



● Functionally complete, awaiting merge

The join sequence, sign-in, role-aware routing and the admin verification queue are built and passing every automated check. Greencubes delivered overnight, and their backend now has real server-side security in it. We checked that ourselves this morning rather than taking the summary on trust.

Not live yet, and the difference matters. The frontend pull request is open, not merged, so three Milestone 3 routes still return 404 in production. Greencubes have asked for that commit on the dev preview first so they can verify it, which is the right order.

MILESTONE 4

Directory MVP




● Not started

No work has begun. None. Zero commits, no branch, no sneaky head start.

Explore and the profile screens are Milestone 2 UX running on sample data. Lovely, but not a directory. Production data, connected search, the claim-and-correction workflow and contact routing all live here.

THE BUILD, TURNED OVER

Everything we made, from every angle.



12 member roles

a twelve-role grid,
live

50 states + D.C.

enumerated on Explore

13 routes

returning 200 in
production

3 legacy redirects

301, each to the right
place

45 tests passing

zero failing

7 contrast fixes

measured, not asserted

Milestone 1, the foundation

Milestone 2, the product system
front door

Milestone 3, the

VERIFIED CANNABIS COMMUNITY AND MARKET INTELLIGENCE

One industry. One network. One Bridge.

Connect cannabis brands, dispensaries, cultivators, sales teams, and service partners. Follow industry activity, discover verified operators, and build the right relationships nationwide.

Join the verified network →

Explore cannabis businesses

50


State discovery

03

Audience controls

B2B

EIN aware access

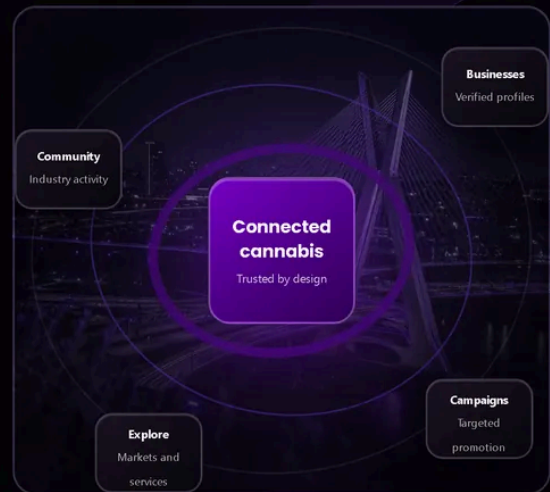

Home · captured live from production, 3 September 2026


Looks finished. Isn't finished.

Every screen on the review build runs against a typed mock adapter, and every screen says so, on the page. That was on purpose. It let you judge the product before a single dollar of backend cost was committed.

Turning mock mode off is one environment variable. As of this morning the backend origin is known and answering, so what is left is the merge and a dev preview deploy to verify against.

- ✓ Explore says its sample records are limited and favourites stay on your device.
- ✓ Create says drafts and library actions stay local until the production API is connected.
- ✓ My Profile says the email reminder integration is pending.

Nothing on the review build implies a capability that isn't there. That was the whole discipline.

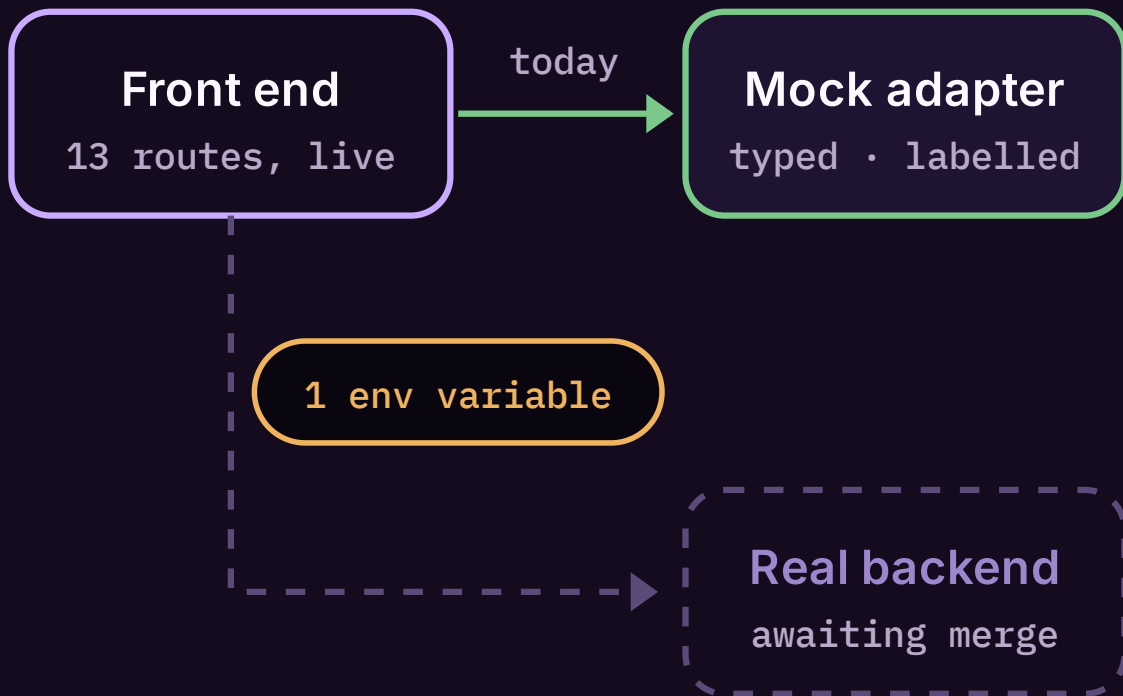

THE RECEIPTS WALL

Twelve numbers, each one checked by hand this morning.

Nothing carried forward from an older report. Every figure below was probed, counted or re-run on 3 September.

13

routes returning 200 in production

45

automated tests passing, zero failing

12

member roles defined and built

36

static pages in the production build

7

contrast failures found and fixed

3

themes checked for AA compliance

77

commits on the development branch

15/9

pull requests opened, then merged

2

deploy environments running

3

legacy paths redirecting correctly

50+

states plus D.C. on Explore

0

client acceptances recorded with a date




That last one isn't a joke and it isn't a complaint. It's just the honest count, and it's the easiest number on this wall to change.

THE FIVE ROUTES WAITING ON YOU

**Milestone 2, in five
polaroids.**






Home

A compact product introduction with legal cannabis positioning, one primary join action, and one-click access to the four main spaces.


PENDING TORI



Community News

The same items as either a visual News Grid or a classic chronological feed, with category and state controls, favourites, and an explicit selected state. Non-algorithmic by design for the MVP.


PENDING, DEFAULT VIEW
UNDECIDED



Create

Promotion and message composition: content type, upload validation, multi-audience selection, live preview, and a guardrail that strips protected detail out of public targeting automatically.


PENDING TORI



My Profile

Two projections of one record, Public and B2B verified, with protected sales and accounting contacts, no public EIN, and a required first-login and monthly contact confirmation.

PENDING TORI



Explore

Nationwide discovery across all fifty states and D.C., with category and role filters, a visible result count, persisted favourites, and a permissioned introduction request.

PENDING TORI

All five were sent for sign-off on 17 August. A review was promised on the 18th, again on the 23rd, and again on 1 September. On 21 August we wrote to the team, in writing, that these routes are not officially approved yet. That is still true, and this page holds to it.


THREE THINGS NOBODY WILL EVER NOTICE

The unglamorous work, briefly glamorised.

Client routing is presentation. Never permission.

Sign-in sends members to their profile and administrators to the admin workspace. The return-path parameter accepts only same-origin paths. Absolute URLs and protocol-relative hosts get rejected. And every routing rule carries an explicit note that the API must still enforce it anyway.


No token in browser storage. The session is read from the API on each load, as a cookie session requires. There is a test that fails if any client file so much as touches web storage.

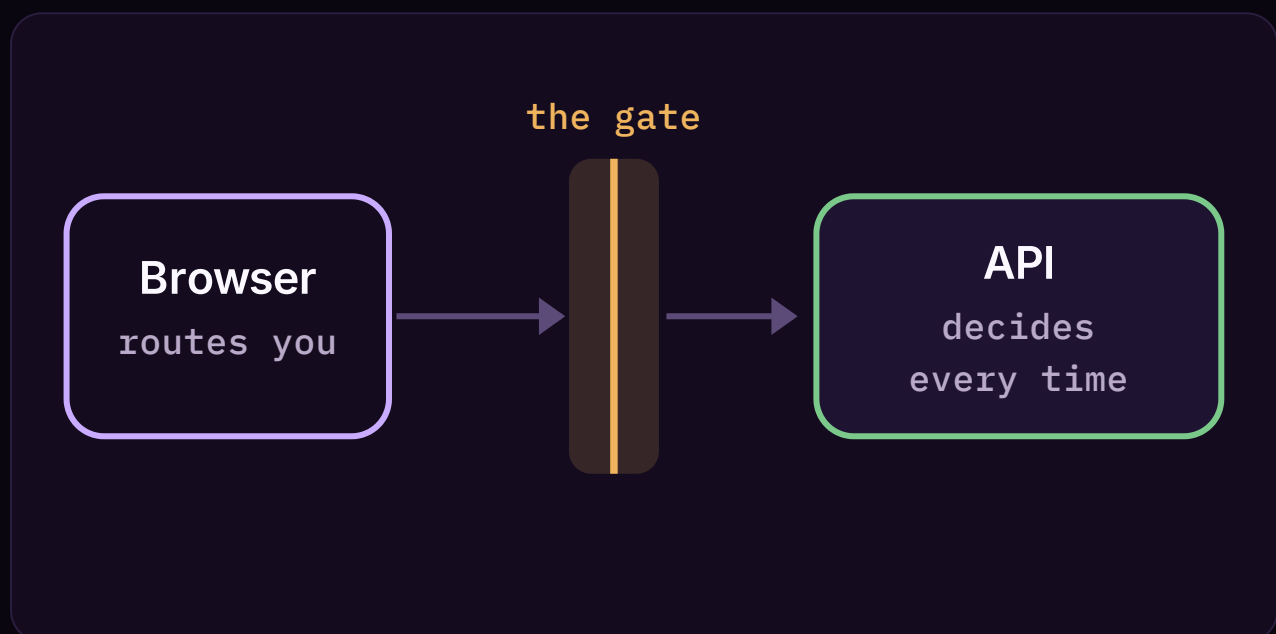

Contrast measured, not asserted.

An automated check implements the published contrast formulas, reads the colour tokens straight out of the stylesheet so the measured values can never drift from what actually ships, and asserts the AA threshold for every text-on-background pair, in all three themes.


Five failures in the admin panel, the worst at 2.88:1 against a 4.5:1 requirement. Two more hiding in the existing theme tokens that nobody knew about, including form error text at 2.22:1, which is to say effectively invisible. It now measures 6.02:1.

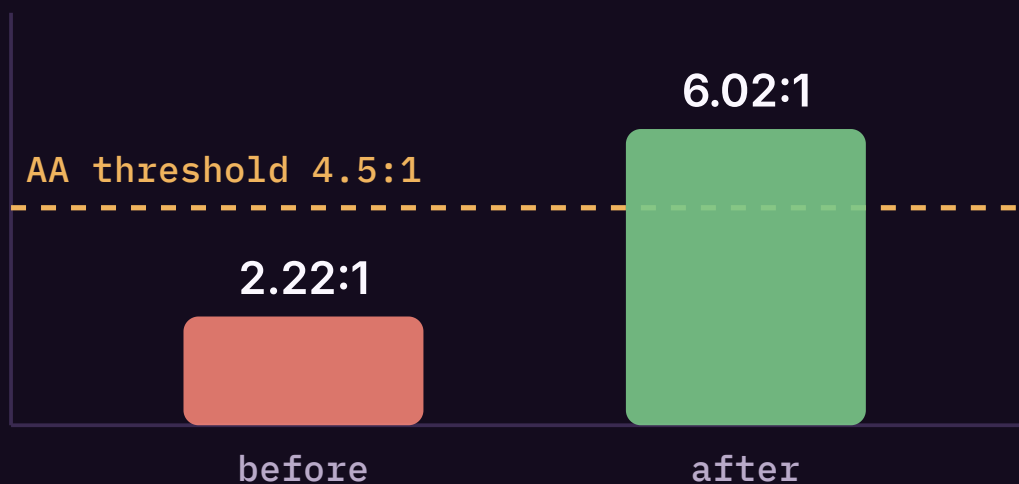

One HTTP client. One contract.

Registration, sign-in and sign-out went into the same typed client every other call already used, so they inherit one base URL, one status mapping and one error type. A second, parallel client that had quietly bypassed all of that got folded back in.

Error text is filtered too: only a curated, human message reaches the screen. A stack trace or a raw backend string physically cannot get in front of a member.

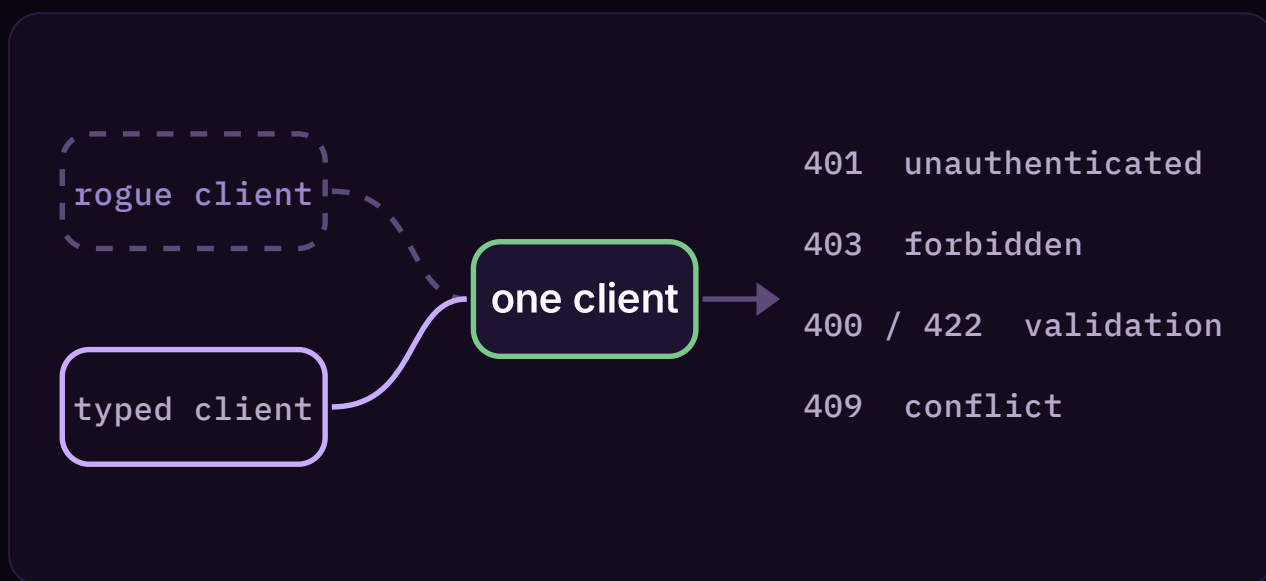

REWRITTEN THIS MORNING, AFTER GREENCUBES DELIVERED

The cookie decision landed. Both rules held.

Greencubes shipped overnight. We went and checked it ourselves rather than taking the summary on trust, and it holds up. This is the good news section, and it is genuinely theirs.

- ✓ The one missing response header is now present, so credentialed cookie sessions work and the test that was failing because of it is no longer blocked.
- ✓ The session endpoint and the identity endpoint both reject an unauthenticated caller with a 401. Server-side enforcement is real, not a client convention.

- ✓ Browser storage for tokens is gone from the frontend. The file that held it no longer exists.
- ✓ The duplicate HTTP client is gone too, so authentication finally routes through the one typed client with the one error contract.
- ✓ The reference join sequence was adopted rather than rebuilt, and Step 2 now lives at its own route.

Those last two are the exact rules we set out in the section above, checked against somebody else's code. They held.

Greencubes additionally report that sign-in issues secure cookies, that sign-out clears them and revokes the refresh session, that the session endpoint returns 401 afterwards, and that role enforcement stays server-side. Those are their words rather than our measurement, and this page marks the difference deliberately.

One item is still open and it is small: a four-line pointer in the project instructions file still names the old repository instead of the current frontend one. Past that, the only reason none of this is live is that the pull request is open and unmerged.



A WORD FROM THE INTERN

"I read all thirteen pages so you don't have to."

You should still read them. He's a robot, he has nothing else on.

He is also legally obliged to mention that Bridge is a platform for the legal cannabis industry, that every route sits behind a 21+ confirmation before entry, and that the 21+ rule was not a design flourish. It came straight out of your own legal and compliance strategy document.

he does watch your cursor. sorry.

MILESTONE 3, THE PART WITH A WAITING ROOM

The admin verification queue, doing its unglamorous job.


Real case rows showing organization, type, market, status and days waiting, with a sortable order and a live count. Running on a clearly-labelled sample queue, exactly as it does in the product.

Verification queue


6 cases awaiting review · sorted by days waiting

ORGANIZATION	TYPE	MARKET	STATUS	DAYS WAITING
Cedar & Coast Cultivation	Cultivator	California	In review	14
Northline Distribution	Distributor	Michigan	In review	12
Halcyon Wellness Co.	Brand	Colorado	Evidence requested	9
Third Street Dispensary	Retailer	Illinois	In review	6
Ridgeway Testing Labs	Testing lab	Massachusetts	Verified	3
Beacon Route Logistics	Transport	Maryland	Evidence requested	2


Sample data. Case detail, meaning the evidence, the decision reasons and the confirmation step, needs the backend's verification-case contract, which has not been supplied yet.

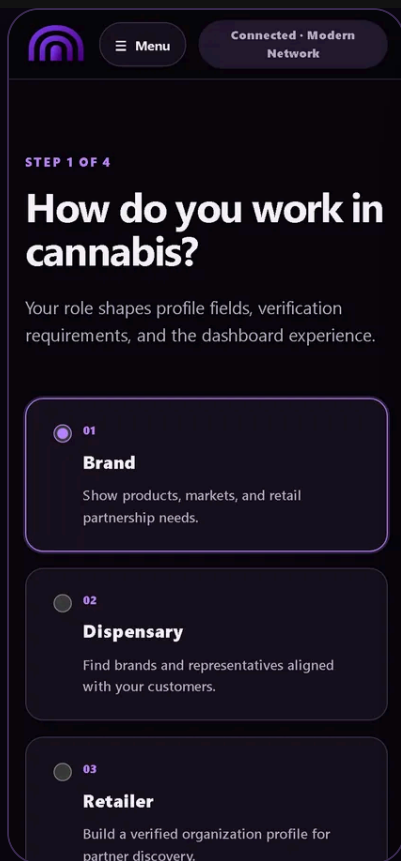

Join · 390 px

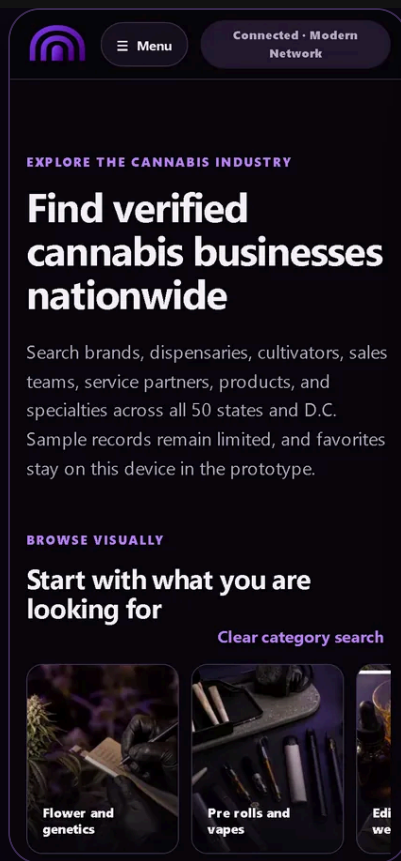

Explore · 390 px



Community News · 390 px



*every route captured
twice, at 1440 px and
390 px, same day.
nothing scrolls sideways.*

FOUR STEPS, TWO OF THEM WAITING ON A HUMAN

**The join sequence,
honestly labelled.**


STEP 1 OF 4

/join

Pick your role

A twelve-role grid with per-role next-step titles and requirements, the founding-member callout, and a boundary note explaining what Steps 2 to 4 will need.

● Live in production



captured live, 3 Sept

STEP 2 OF 4

/join/account

Create the account

Display name, email, password and confirmation, showing the role you chose in Step 1 with a link back to change it. Full inline validation and error states.

● Built · pending merge

STEP 3 OF 4

no route yet

Organization details

Legal name, public name, EIN, licence, location and contact owner. Needs organization-scoped draft persistence, which is backend-owned.

● Awaiting backend + approval

STEP 4 OF 4

no route yet

Verification evidence

Server-created upload intents, document scanning, a redacted review summary and a verification case.

● Awaiting backend + approval

Steps 3 and 4 aren't missing routes and they aren't a hosting problem. Real member identity now exists, which was the largest of the four backend pieces. What is still outstanding is organization-scoped drafts, protected evidence storage and a review case, plus a product answer on what evidence each of the twelve roles must supply and what the public "Verified" badge actually promises.

Three decisions and a nod. That's the whole list.

1

Route-by-route: accept or revise

All five Milestone 2 routes. A dated yes-or-revise, in writing. This is the outstanding acceptance and it unblocks nearly everything downstream.

2

Join Step 2 and Step 4

Product approval, with Melissa. Until that lands, those screens are not represented as client-approved anywhere, including here.

3

Community News, by default

News Grid, or the classic chronological feed? Both are built. One of them has to open first.

And when you have a spare afternoon

- ✓ What evidence each of the twelve roles must supply for verification.
- ✓ Which profile and contact fields are public, member-only or protected.
- ✓ Formal brand approval of the purple direction already running in production.
- ✓ What the public "Verified" badge promises.
- ✓ First market and priority role for launch.

THE SINGLE MOST USEFUL THING THAT CAN HAPPEN THIS WEEK



A dated, written accept-or-revise on the five review routes. Join Steps 3 and 4, the directory work, the verification policy. All of it is currently waiting behind a product decision rather than behind engineering capacity.

The build is ready for it.



BRIDGE

Connect. Grow. Fight Together.

**This is the companion.
The report is the record.**

Every claim and figure on this page maps back to the Bridge Milestones 1 to 3 Delivery Report and its evidence index. Where the report says something is unfinished, this page says it too, in a slightly sillier font.

21+

Bridge is a platform for the **legal cannabis industry**. Every route sits behind a 21+ confirmation before entry, exactly as the live product does. Please enjoy responsibly, and in line with the laws of your state.

Prepared by Momentum Digital · 3 September 2026 · Covering contract Milestones 1, 2 and 3. Confidential, for client review. No pricing, totals or payment terms appear on this page.
